

COMMONWEALTH OF VIRGINIA
DEPARTMENT OF HIGHWAYS AND TRANSPORTATION

June 5, 1986

Project 0123-029-000, C-501
Roadways Adjacent to the
CIA Headquarters at Langley
Fairfax County

Mr. John P. Fowler, II, P. E.
Dewberry & Davis
8401 Arlington Boulevard
Fairfax, Virginia 22031

Dear Mr. Fowler:


Reference is made to your letter of May 28 which included a revised project schedule and May 29 regarding the supplemental work that has been performed in connection with the CIA Traffic Advisory Committee meetings.

The revised project schedule appears realistic, however, the mid-August completion date hinges on the utility field inspection plans and the success of the CIA in scheduling and holding the remaining two TAC meetings. I am forwarding a copy of this schedule to Mr. [redacted] for his information. The utility information being secured by So-Deep will be forwarded to you as soon as it is received.

STAT

Your letter outlines the supplemental design work that has been performed to resolve issues raised at the TAC meetings. Hopefully no further studies will be required and the project can be completed within the existing budget.

Sincerely,



H. M. Shaver, Jr.
State Location and
Design Engineer

cc: [redacted]

w/enclosure

STAT

Sanitized Copy Approved for Release 2011/07/18 : CIA-RDP89-00244R001403340012-9

Page Denied

Dewberry & Davis



Engineers
Architects
Planners
Surveyors

8401 Arlington Boulevard
Fairfax, VA 22031
703 849-0100

May 28, 1986

Mr. H.M. Shaver, Jr.
State Location & Design Engineer
Commonwealth of Virginia
Department of Highways & Transportation
1221 East Broad Street
Richmond, Virginia 23219

Re: CIA Access Improvements - Phase II
Progress Report #9 - through April 1986

LOCATION AND DESIGN DIVISION RECEIVED			
HMS	MAY 30 1986		SBA
ECC			NAS
DDH	LRM	FBB	LPW
JEY	RAM	CFB	FILE

Dear Mr. Shaver:

Respectfully submitted is our Progress Report describing professional engineering services provided the Department on the referenced Project during April. Accompanying this narrative is a revised Project Schedule and a numerical representation of the status of the various work tasks comprising the assignment.

Field Surveys and Mapping

Tasks previously completed.

Preliminary Layout

A second Technical Advisory Committee Meeting to discuss the three alternative designs was held April 14th. Subsequently, we were advised to complete the Field Inspection Plans based upon the recommended design reviewed at the April meeting.

Field Inspection Plans

Services provided in April consisted of development of the preliminary maintenance of traffic plan, completion of the traffic control plans for incorporation into the Field Inspection set, and effort on development of the Field Inspection Plans. Field Inspection submittal was scheduled for May 19th with the date for the field inspection itself set for June 5th.

Public Participation Program

As noted, a second meeting of the CIA's Traffic Advisory Committee was held in April. At that time, three alternative designs for the Route 193/Route 123 intersection were discussed.

Fairfax, VA
Annapolis, MD
Baltimore, MD
Danville, VA

Gaithersburg, MD
Landover, MD
Marion, VA
Morristown, TN

Raleigh, NC
Richmond, VA
Woodbridge, VA

Mr. H.M. Shaver, Jr.

Page -2-

May 28, 1986

Concluding Statement

Good progress was made the latter part of April on Field Inspection Plans for the Project. Field Inspection has been scheduled for June 5th with plan delivery to occur late in May.

Our proposed Schedule for completing this design assignment is attached to this Report.

Yours very truly,

DEWBERRY & DAVIS



John P. Fowler, II, P.E.
Managing Principal

JPF:rad
Attachments

Dewberry & Davis




CIA ACCESS IMPROVEMENTS - PHASE II
Fairfax County, Virginia
State Project: 0219-A-002

WORK STATUS SUMMARY

Tasks	Weighted Value (%)	Actual Percent Complete		Scheduled Percent Complete	
		Task	Total	Task	Total
A. Field Survey	13.2	100	13.2	100	13.2
B. Base Mapping	3.1	100	3.1	100	3.1
C. Preliminary Layout	8.2	100	8.2	100	8.2
D. Preliminary Traffic Control	4.6	100	4.6	100	4.6
E. Preliminary Maintenance of Traffic	2.7	100	2.7	100	2.7
F. Preliminary Landscaping	4.1	100	4.1	100	4.1
G. Field Inspection Plans	25.3	90	22.8	100	25.3
H. Final Plans & Specifications	35.0	---	---	60	35.0
I. Public Meetings	3.8	33	<u>1.3</u>	67	<u>3.8</u>
TOTALS	100.0		60.0		100.0

CIA ACCESS IMPROVEMENTS
PHASE II - FINAL DESIGN AND CONSTRUCTION DOCUMENTS
SCHEDULE

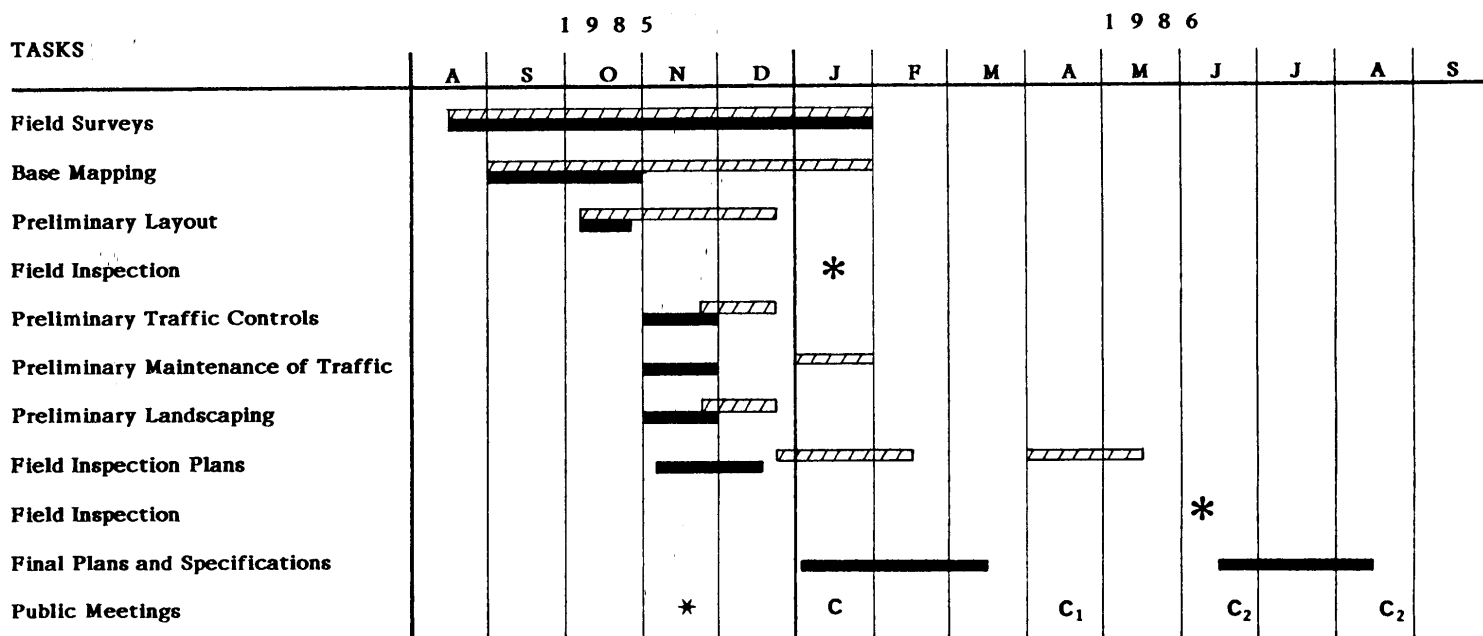

- * Field Inspections
- C Advisory Committee Meetings
- * Meeting rescheduled to January
- C₁ Second Initial Meeting
- C₂ Rescheduled Advisory Committee Meetings
